


PRELIMINARY SCHEDULE - 249A, 250, 251, 252, 253, 254, 254 A&B, 255, 255A, 256, CORRIDORS
 DEMO & ABATEMENT
 CLASSROOM RENOVATION - ROOF

ID	Task Mode	Task Name	Duration	Start	Finish	Resource Names	% Complete	1st Quarter				2nd Quarter	
								Dec	Jan	Feb	Mar	Apr	
1	✓	Viking Install Hard Barriers	1 day	Mon 12/16/19	Mon 12/16/19	Viking	100%						
2	✓	Containment 1-Rooms 253, 254, 254A, 254B, 255, 255A,256&	3 days	Mon 12/16/19	Wed 12/18/19	AAIS	100%						
3	✓	Remove Ceiling Tiles	1 day	Wed 12/18/19	Wed 12/18/19	AAIS	100%						
4	✓	Demo Sheetrock Ceilings254A&&255A	1 day	Thu 12/19/19	Thu 12/19/19	AAIS	100%						
5	✓	Wipe Clean	1 day	Fri 12/20/19	Fri 12/20/19	AAIS	100%						
6	✓	Cleaned	1 day	Fri 12/20/19	Fri 12/20/19	AAIS	100%						
7	✓	Demo	2 days	Mon 12/23/19	Tue 12/24/19	AAIS	100%						
8	✓	Corridor Grid, BR Ceiling Framing & Criticals around unit ventilators	1 day	Thu 12/26/19	Thu 12/26/19	AAIS	100%						
9	✓	Cut 3x3 openings for Sprinklers	2 days	Fri 12/27/19	Mon 12/30/19	AAIS	100%						
10	✓	Clean 1 st containment	1 day	Tue 12/31/19	Tue 12/31/19	AAIS	100%						
11	✓	Make Safe for Plaster Ceiling Removal	2 days	Fri 1/3/20	Mon 1/6/20	Viking	100%						
12	✓	Hanging Ductwork	2 days	Fri 1/3/20	Mon 1/6/20	Viking	100%						
13	✓	Water Lines	2 days	Fri 1/3/20	Mon 1/6/20	Viking	100%						
14	✓	Sprinklers	2 days	Fri 1/3/20	Mon 1/6/20	Viking	100%						
15	✓	Electric & Data Wires	2 days	Fri 1/3/20	Mon 1/6/20	Viking	100%						
16	✓	Anchor Lights	2 days	Fri 1/3/20	Mon 1/6/20	Viking	100%						
17	⚠	AAIS Remove Plaster Ceilings CR & Corridor-Floorngs, Univentilators	10 days	Tue 1/7/20	Mon 1/20/20	AAIS	0%						
18	⚠	Clearance	2 days	Tue 1/21/20	Wed 1/22/20	AAIS	0%						
19	⚠	VIKING COMPLETE ROOMS	21 days?	Thu 1/23/20	Thu 2/20/20		0%						
20	⚠	UL Rating	8 days	Thu 1/23/20	Mon 2/3/20	Viking	0%						
21	⚠	Subfloors	10 days	Fri 1/24/20	Thu 2/6/20	Viking	0%						
22	⚠	Plumber	10 days	Tue 1/28/20	Mon 2/10/20	Viking	0%						
23	⚠	HVAC	10 days	Tue 1/28/20	Mon 2/10/20	Viking	0%						
24	⚠	Pipe Insulatio/Duct Wrap	8 days	Tue 1/28/20	Thu 2/6/20	Viking	0%						
25	⚠	Flooring	5 days	Fri 2/7/20	Thu 2/13/20	Viking	0%						
26	⚠	Painting	8 days	Fri 2/7/20	Tue 2/18/20	Viking	0%						
27	⚠	Final Inspections	1 day	Wed 2/19/20	Wed 2/19/20	Viking	0%						
28	⚠	Clean up	2 days?	Wed 2/19/20	Thu 2/20/20	Viking	0%						
29													
30	✓	Hard Barriers Containment 2	1 day	Mon 12/16/19	Mon 12/16/19	Viking	100%						
31	⚠	Containment 2 - 252, 251, 250,249 and 249A& Corridors-Demo & Abatement	5 days	Thu 1/2/20	Wed 1/8/20	AAIS	0%						
32	⚠	Remove Ceiling Tiles	2 days	Thu 1/9/20	Fri 1/10/20	AAIS	0%						
33	⚠	Demo Sheetrock	1 day	Mon 1/13/20	Mon 1/13/20	AAIS	0%						
34	⚠	Ceilings and Grid	4 days	Tue 1/14/20	Fri 1/17/20	AAIS	0%						
35	⚠	Wipe Clean	1 day	Mon 1/20/20	Mon 1/20/20	AAIS	0%						
36	⚠	Clearance	1 day	Tue 1/21/20	Tue 1/21/20	AAIS	0%						
37	⚠	Demo	2 days	Wed 1/22/20	Thu 1/23/20	AAIS	0%						

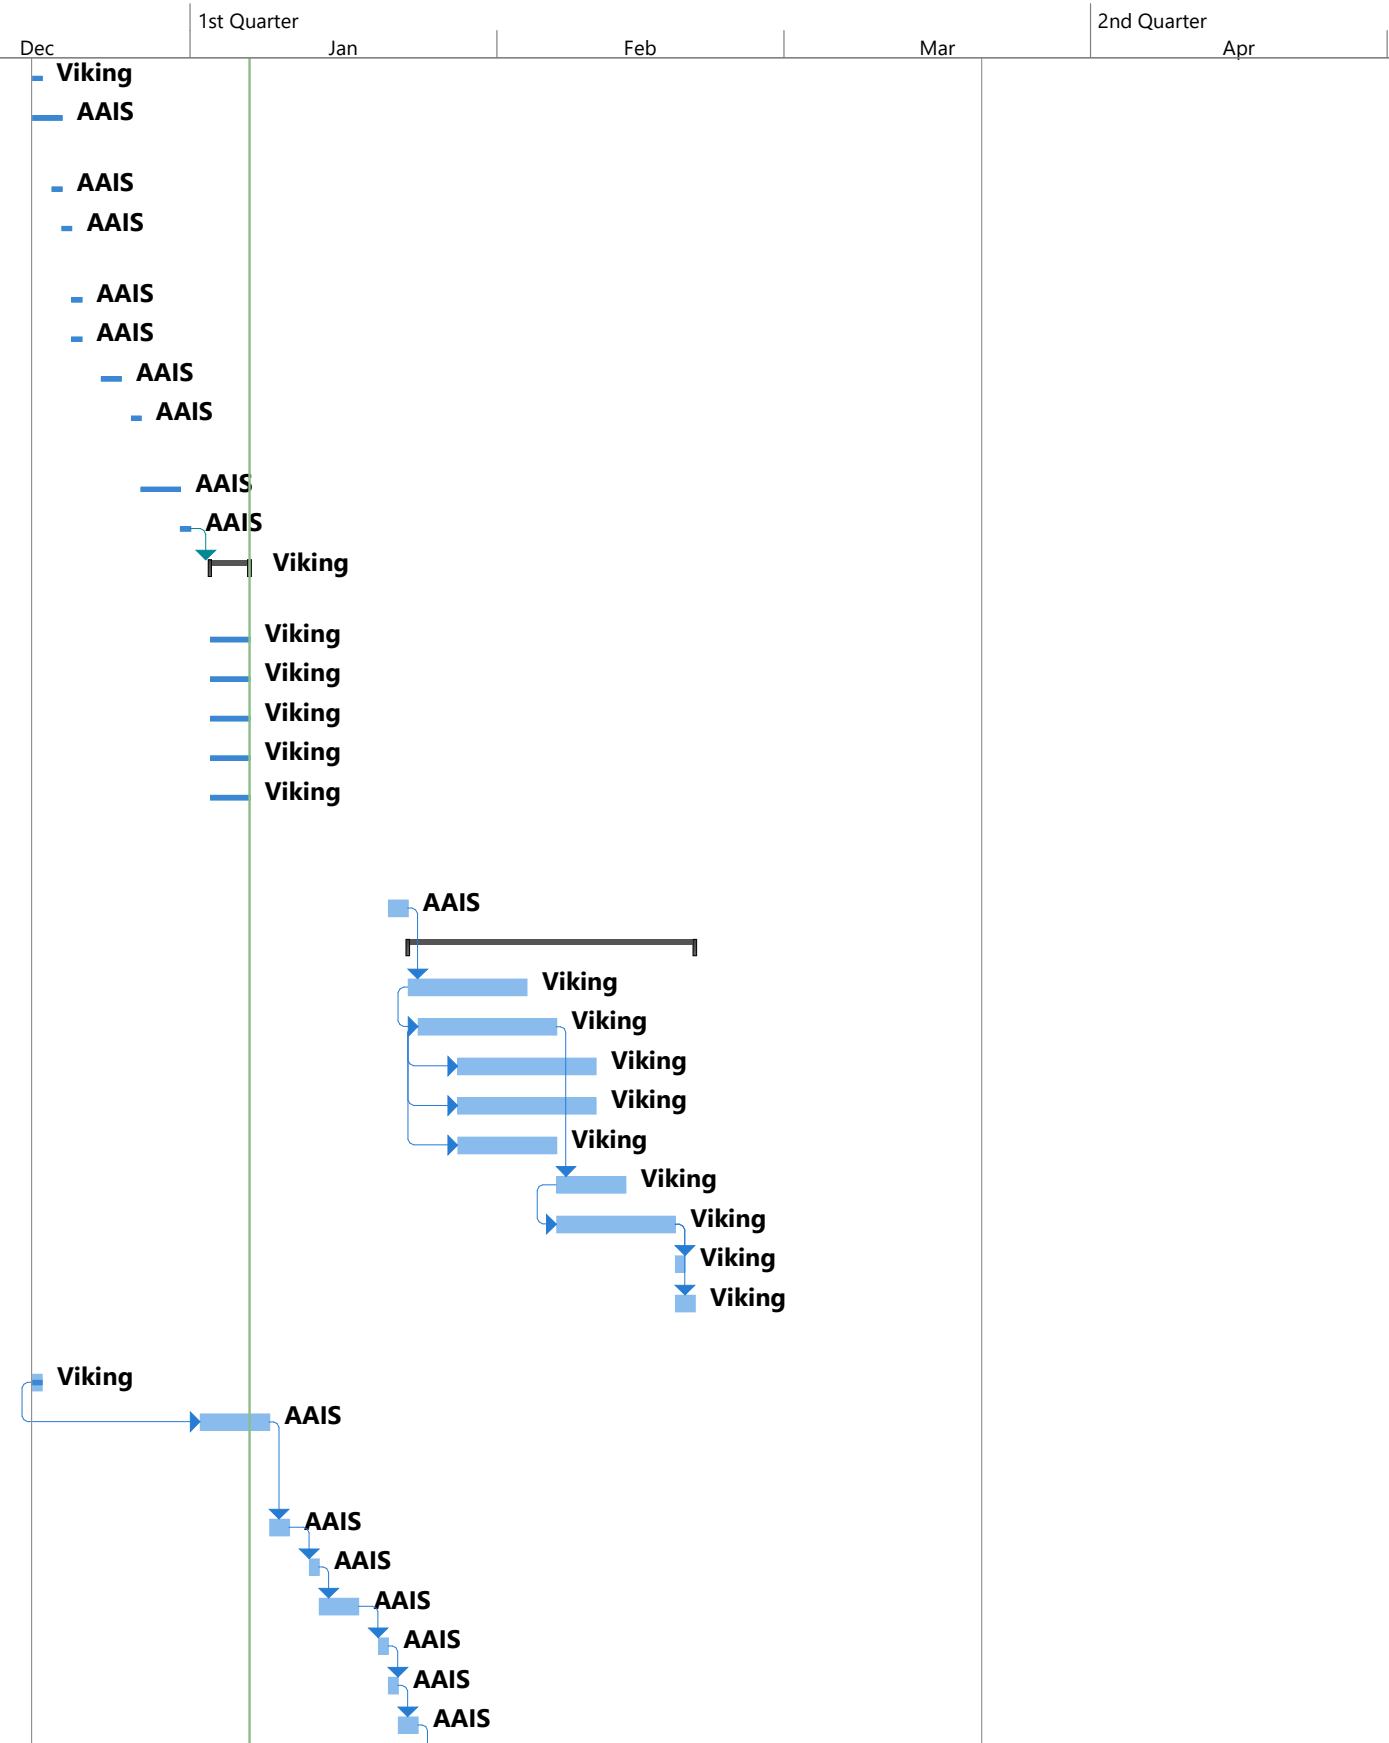

Project: Classroom Upd
 Date: Tue 1/7/20

Task Split Milestone Summary Project Summary Progress Manual Progress

PRELIMINARY SCHEDULE - 249A, 250, 251, 252, 253, 254, 254 A&B, 255, 255A, 256, CORRIDORS
 DEMO & ABATEMENT
 CLASSROOM RENOVATION - ROOF

ID	Task Mode	Task Name	Duration	Start	Finish	Resource Names	% Complete	1st Quarter				2nd Quarter		
								Dec	Jan	Feb	Mar	Apr		
38		Corridor Grid, Ceiling Framing & Criticals Around Unit Ventilators	2 days	Fri 1/24/20	Mon 1/27/20	AAIS	0%							
39		Cut Opening for Sprinklers	2 days	Tue 1/28/20	Wed 1/29/20	AAIS	0%							
40		Clean 2nd Containment	2 days	Thu 1/30/20	Fri 1/31/20	AAIS	0%							
41		Make Safe for Plaster Ceiling Removal	3 days	Mon 2/3/20	Wed 2/5/20		0%							
42		AAIS Remove Plaster Ceilings CR & Corridor-Floors, Univents	10 days	Thu 2/6/20	Wed 2/19/20	AAIS	0%							
43		Clearance	2 days	Thu 2/20/20	Fri 2/21/20	AAIS	0%							
44		VIKING COMPLETE ROOMS	20 days	Mon 2/24/20	Fri 3/20/20		0%							
45		UL Rating	8 days	Mon 2/24/20	Wed 3/4/20	Viking	0%							
46		Subfloors	10 days	Tue 2/25/20	Mon 3/9/20	Viking	0%							
47		Plumber	10 days	Thu 2/27/20	Wed 3/11/20	Viking	0%							
48		HVAC	10 days	Thu 2/27/20	Wed 3/11/20	Viking	0%							
49		Pipe Insulatio/Duct Wrap	8 days	Thu 2/27/20	Mon 3/9/20	Viking	0%							
50		Flooring	5 days	Tue 3/10/20	Mon 3/16/20	Viking	0%							
51		Painting	8 days	Tue 3/10/20	Thu 3/19/20	Viking	0%							
52		Final Inspections	1 day	Fri 3/20/20	Fri 3/20/20	Viking	0%							
53		Clean Up	1 day	Fri 3/20/20	Fri 3/20/20	Viking	0%							
54														
55		ROOF SCHEDULE	1 day?	Mon 12/16/19	Mon 12/16/19		0%							

Project: Classroom Upd
 Date: Tue 1/7/20

Task Split Milestone Summary Project Summary Progress Manual Progress
