


DAVENPORT ELEMENTARY SCHOOL CLASSROOMS 6 AND 7

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Jan 5, '20							Jan 12, '20				
							S	M	T	W	T	F	S	S	M	T	W	
1		CLASSROOMS 6 AND 7	25 days?	Tue 1/7/20	Mon 2/10/20													
2		Meyers Move Furniture	1 day	Tue 1/7/20	Tue 1/7/20													
3		Demo Prep For Abatement	3 days	Tue 1/7/20	Thu 1/9/20	2SS												
4		Abatement	2 days	Fri 1/17/20	Mon 1/20/20	3SS+8 days												
5		Clearance/Breakdown	1 day	Mon 1/20/20	Mon 1/20/20	4FF												
6		Put Back Classrooms	16 days?	Mon 1/20/20	Mon 2/10/20													
7		Framing/Ins. Ext. Walls	1 day	Mon 1/20/20	Mon 1/20/20	5SS												
8		Framing Blocking	1 day	Tue 1/21/20	Tue 1/21/20	7												
9		Rough MEPS	1 day	Wed 1/22/20	Wed 1/22/20	8												
10		Rough Inspection	1 day	Wed 1/22/20	Wed 1/22/20	9SS												
11		Sheetrock Rooms	1 day	Thu 1/23/20	Thu 1/23/20	10												
12		Start Taping	3 days	Fri 1/24/20	Tue 1/28/20	11												
13		2nd/3rd coat taping	2 days	Mon 1/27/20	Tue 1/28/20	12FS-2 days												
14		Clean up/VCT Install	1 day	Tue 1/28/20	Tue 1/28/20	13SS+1 day												
15		Paint/Ceiling/Misc. Carp.	4 days	Wed 1/29/20	Mon 2/3/20	14												
16		Millwork	2 days	Fri 1/31/20	Mon 2/3/20	15SS+2 days												
17		Finish MEPS	3 days	Mon 2/3/20	Wed 2/5/20	16SS+1 day												
18		Final Inspections	1 day	Thu 2/6/20	Thu 2/6/20	17												
19		Custodian Wax/Strip Floors	1 day	Fri 2/7/20	Fri 2/7/20	18												
20		Move Back	1 day?	Mon 2/10/20	Mon 2/10/20	19												

Project: Update 1-28.mpp
Date: Tue 1/28/20

Task		Summary		Manual Task		Start-only	
Milestone		Project Summary		Manual Summary		Finish-only	

DAVENPORT ELEMENTARY SCHOOL CLASSROOMS 6 AND 7

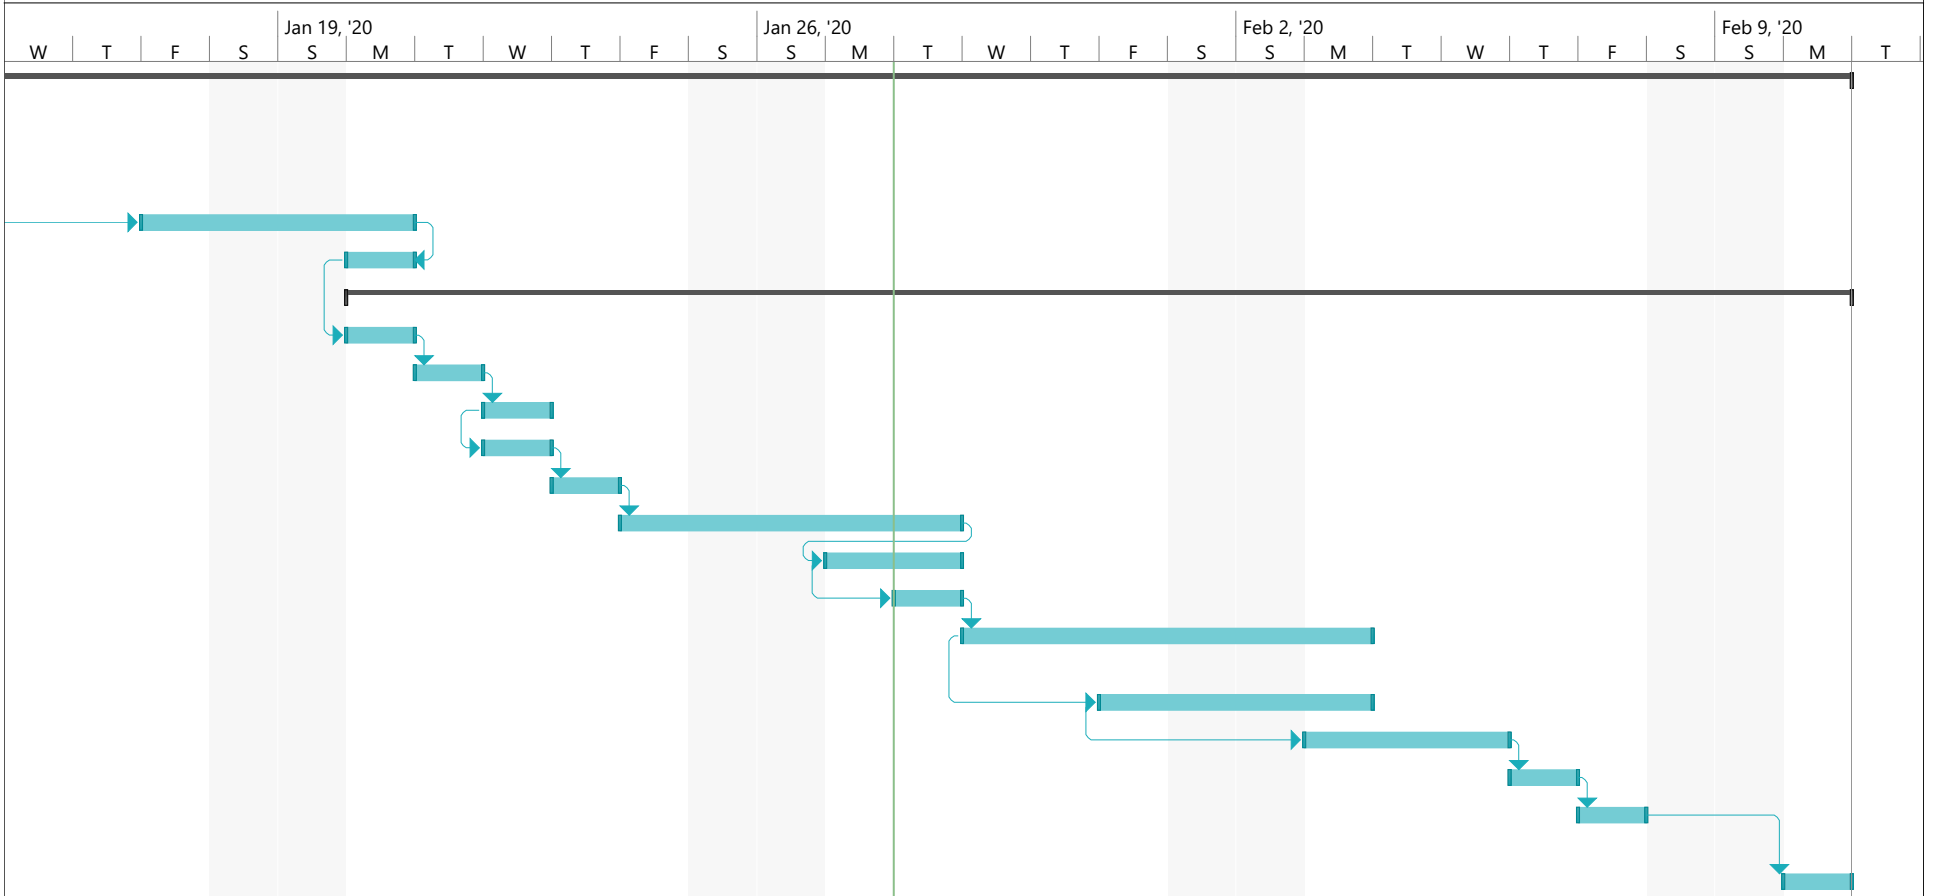

Project: Update 1-28.mpp
Date: Tue 1/28/20

Task		Summary		Manual Task		Start-only	
Milestone		Project Summary		Manual Summary		Finish-only	
